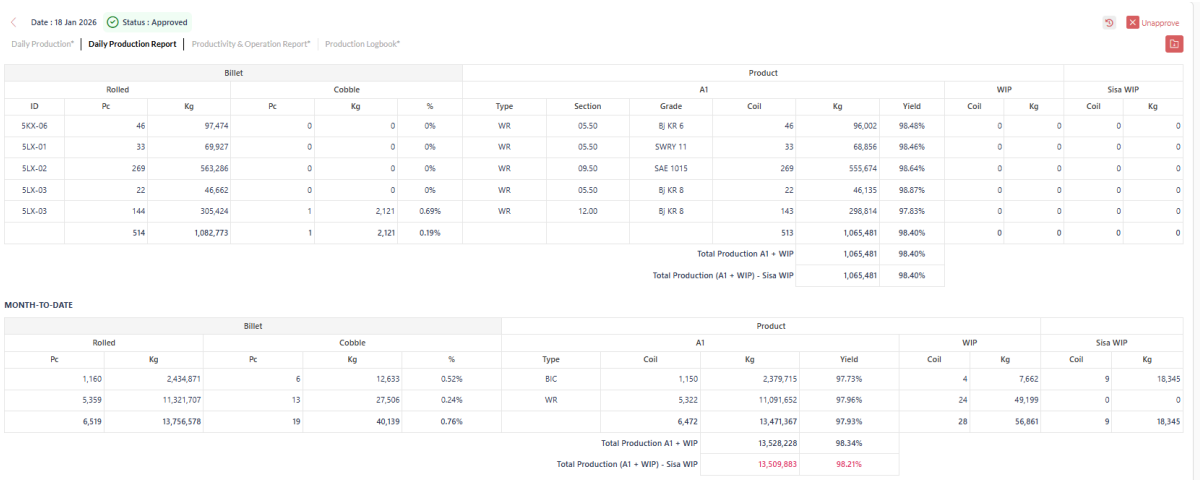


Date : 18 Jan 2026 | Status : Approved | Unapprove

Daily Production* | **Daily Production Report** | Productivity & Operation Report* | Production Logbook*

Billet						Product									
Rolled			Cobble			A1						WIP		Sisa WIP	
ID	Pc	Kg	Pc	Kg	%	Type	Section	Grade	Coil	Kg	Yield	Coil	Kg	Coil	Kg
5KX-06	46	97,474	0	0	0%	WR	05.50	Bj KR 6	46	96,002	98.48%	0	0	0	0
5LX-01	33	69,927	0	0	0%	WR	05.50	SWRY 11	33	68,856	98.46%	0	0	0	0
5LX-02	269	563,286	0	0	0%	WR	09.50	SAE 1015	269	555,674	98.64%	0	0	0	0
5LX-03	22	46,662	0	0	0%	WR	05.50	Bj KR 8	22	46,135	98.67%	0	0	0	0
5LX-03	144	305,424	1	2,121	0.69%	WR	12.00	Bj KR 8	143	298,814	97.83%	0	0	0	0
	514	1,082,773	1	2,121	0.19%				513	1,065,481	98.40%	0	0	0	0
								Total Production A1 + WIP		1,065,481	98.40%				
								Total Production (A1 + WIP) - Sisa WIP		1,065,481	98.40%				

MONTH-TO-DATE

Billet					Product							
Rolled		Cobble			A1				WIP		Sisa WIP	
Pc	Kg	Pc	Kg	%	Type	Coil	Kg	Yield	Coil	Kg	Coil	Kg
1,160	2,434,871	6	12,633	0.52%	BIC	1,150	2,379,715	97.73%	4	7,662	9	18,345
5,359	11,321,707	13	27,506	0.24%	WR	5,322	11,091,652	97.96%	24	49,199	0	0
6,519	13,756,578	19	40,139	0.76%		6,472	13,471,367	97.93%	28	56,861	9	18,345
						Total Production A1 + WIP	13,528,228	98.34%				
						Total Production (A1 + WIP) - Sisa WIP	13,509,883	98.21%				

DAILY PRODUCTION REPORT

18-Jan-26

	BILLET						PRODUCT							
	Rolled			*Cobble*			*A1*						*WIP*	
	ID	*Pc*	*Kg*	*Pc*	*Kg*	*%*	*Type*	*Section*	*Grade*	*Coil*	*Kg*	*Yield*	*Coil*	*Kg*
7	5LX-03	22	46,662				WR	5,5	Bj KR 8	22	46,135	98,87%		
8	5LX-02	269	563,286				WR	9,5	SAE 1015	269	555,674	98,65%		
9	5LX-03	144	305,424	1,0	2,121,0	0,69%	WR	12,0	Bj KR 8	143	298,814	97,84%		
10	5KX-06	46	97,474				WR	5,5	Bj KR 6	46	96,002	98,49%		
11	5LX-01	33	69,927				WR	5,5	SWRY 11	33	68,856	98,47%		
12							WR					#DIV/0!		
13							WR					#DIV/0!		
14							WR					#DIV/0!		
15							WR					#DIV/0!		
16		**514,0**	**1,082,773,0**	**1,0**	**2,121**	**0,20%**				**513**	**1,065,481**	**98,40%**	**0**	**-**
17									**Total Production A1 + WIP**		**1,065,481**	**98,40%**		


MONTH-TO-DATE

	BILLET						PRODUCT							
	Rolled			*Cobble*			*A1*						*WIP*	
	Pc	*Kg*	*Pc*	*Kg*	*%*	*Type*				*Coil*	*Kg*	*Yield*	*Coil*	*Kg*
22	5,359,0	11,321,707,0	13,0	27,506,0	0,24%	WR				5,322,0	11,091,652,0	97,97%	24,0	49,199,0
23	1,160,0	2,434,871,0	6,0	12,633,0	0,52%	BIC				1,150,0	2,379,715,0	97,73%	4,0	7,662,0
24	0,0	0,0	0,0	0,0	#DIV/0!	MIC				0,0	0,0	#DIV/0!	0,0	0,0
25														
26	**6,519,0**	**13,756,578**	**19,0**	**40,139**	**0,29%**					**6,472**	**13,471,367**	**97,93%**	**28**	**56,861**
27									**Total Production A1 + WIP**		**13,528,228**	**98,34%**		

1. Working Time Available	*min*	1,440	25,920
2. Planned Stoppage (a+b+c)	*min*	0	7,200
a. Shut Down	*min*	0	7,200
b. Peak Hour	*min*	0	0
c. Others	*min*	0	0
3. Delay Maintenance (a+b+c)	*min*	224	2,155
a. Daily Maintenance	*min*	0	0
b. Section / Pass / Grade Chang	*min*	207	1,859
c. Section Setting	*min*	17	296
4. Break Down	*min*	32	908
a. Operation	*min*	32	487
b. Mechanical	*min*	0	353
c. Electrical	*min*	0	19
d. Material / Billet Defect	*min*	0	49
e. Un-Controllable	*min*	0	0
5. Production Time Available (1-2)	*min*	1,440	18,720
6. Registered Delay (3+4)	*min*	256	3,063
7. Delay Counter	*min*	259	3,086
8. Slow Rolling (7-6)	*min*	3	23
9. Effective Production Time (5-6-8	*min*	1,181	15,634
10. a. Nett Utilization (9/5)	%	82,0%	83,5%
b. Gross Utilization (9/1)	%	82,0%	60,3%
11. a. Nett Rolling Rate (Billet / (9))	*MT/hour*	55,01	52,79
b. Gross Rolling Rate (Billet / (5	*MT/hour*	45,12	44,09
12. Gas Consumption	*Nmc*	34,132	451,960
	Nmc/ T	32,03	33,41
13. Electricity Consumption	*MWH*	0,0	2,398
	KWH / T	0,00	178,02
14. Water Consumption	*M3*	11	1,613

1. Working Time Available	min	1,440	25,920
2. Planned Stoppage	min	0	7,200
a. Shut Down	min	0	7,200
b. Peak Hour	min	0	0
c. Others	min	0	0
3. Delay Maintenance	min	224	2,155
a. Daily Maintenance	min	0	0
b. Section / Pass / Grade Change	min	207	1,859
c. Section Setting	min	17	296
4. Break Down	min	32	908
a. Operation	min	32	487
b. Mechanical	min	0	353
c. Electrical	min	0	19
d. Material Billet Defect	min	0	49
e. Un-Controllable	min	0	0
5. Production Time Available (1-2)	min	1,440	18,720
6. Registered Delay (3+4)	min	256	3,063
7. Delay Counter	min	259	10,286
8. Slow Rolling (7-6-2)	min	3	23
9. Effective Production Time (5-6-8)	min	1,181	15,634
10. a. Nett Utilization (9/5)	%	82.01%	83.51%
b. Gross Utilization (9/1)	%	82.01%	60.31%
11. a. Nett Rolling Rate (Billet/(9))	MT/Hour	55.00	52.79
b. Gross Rolling Rate (Billet/(5))	MT/Hour	45.11	44.09
12. Gas Consumption	NMC	34,132	451,960
	NMC/T	31	36
13. Electricity Consumption	MWH	0	2,398.41
	KWH/T	0	195.24
14. Water Consumption	M3	11	1,613
	M3/Ton	0.01	0.13

Activate Windows
Go to Settings to activate Windows.

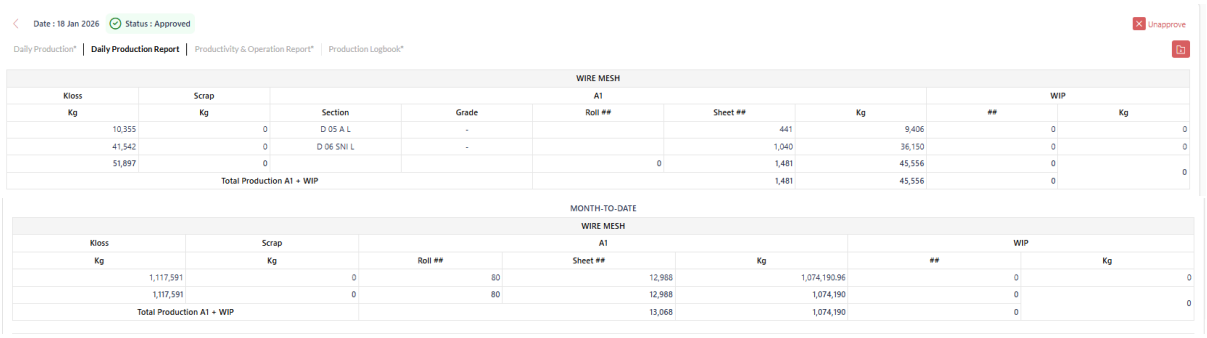

Date : 18 Jan 2026 Status : Approved

Unapprove

Daily Production* | **Daily Production Report** | Productivity & Operation Report* | Production Logbook*

WIRE MESH								
Kloss	Scrap			A1			WIP	
Kg	Kg	Section	Grade	Roll ##	Sheet ##	Kg	##	Kg
10,355	0	D 05 A L	-		441	9,406	0	0
41,542	0	D 06 SNI L	-		1,040	36,150	0	0
51,897	0			0	1,481	45,556	0	0
Total Production A1 + WIP					1,481	45,556	0	

MONTH-TO-DATE

WIRE MESH							
Kloss	Scrap	A1			WIP		
Kg	Kg	Roll ##	Sheet ##	Kg	##	Kg	
1,117,591	0	80	12,988	1,074,190.96	0	0	
1,117,591	0	80	12,988	1,074,190	0	0	
Total Production A1 + WIP			13,068	1,074,190	0		

WIRE MESH

Klos	Scrap			A1			WIP	
Kg	Kg	Section	Grade	##	Kg	Yield 2	##	Kg
10,355		5 A	U50	441	9,407	90,84%		
41,542		6 SNI	U50	1,040	36,150	87,02%		
					0			
-					0			
51,897	0		0	1,481	45,557	87,78%		0
Total Production A1 + WIP				1,481	45,557	87,78%		

MONTH-TO-DATE

WIRE MESH

Klos	Scrap		A1			WIP	
Kg	Kg	Roll ##	Sheet ##	Kg	Yield 2	##	Kg
1,117,591		80	12,988	1,074,191	97,00%		
Total Production A1 + WIP				1,074,191	97,00%		

Section | Grade | ## | Kg

Month To Date

Wire Drawing				
Wire Rod Coil		Drawn Wire Klos		Yield
Coil	Kg	Coil	Kg	
541	1,123,510	556	1,112,908	99.06%

MONTH-TO-DATE

WIRE DRAWING

Wire-Rod Coil			Drawn-Wire Klos			
##	Kg		##	Kg	Yield
541	1,123,510		556	1,112,908	99,06%

1. Working Time Available	*min*	1,440	**25,920**
2. Planned Stoppage (a+b+c)	*min*	240	**14,100**
a. Shut Down	*min*	0	**12,900**
b. Peak Hour	*min*	240	**1,200**
c. Others	*min*	0	**0**
3. Delay Maintenance (a+b+c)	*min*	114	**1,110**
a. Daily Maintenance	*min*	54	**476**
b. Section Change	*min*	60	**572**
c. Section Setting	*min*	0	**62**
4. Break Down	*min*	389	**2,672**
a. Operation	*min*	389	**2,366**
b. Mechanical	*min*	0	**229**
c. Electrical	*min*	0	**77**
d. Material Defect	*min*	0	**0**
e. Un-Controllable	*min*	0	**0**
5. Production Time Available (1-2)	*min*	1,200	11,820
6. Registered Delay (3+4)	*min*	503	3,782
7. Delay Counter	*min*	503	**3,782**
8. Slow Operation (7-6)	*min*	0	**0**
9. Effective Production Time (5-6-8)	*min*	697	8,038
10. a. Nett Utilization (9/5)	%	58,08%	**68,00%**
b. Gross Utilization (9/1)	%	48,40%	**31,01%**
11. a. Nett Productivity (Sheet / (9))	*Sheet/hour*	127,48924	**102,92112**
b. Gross Productivity (Sheet / (5))	*Sheet/hour*	74,05	**69,989848**
12. Electricity Consumption	*MWH*	3,837	54,604
	KWH / T	84,2243	50,8327
13. Water Consumption	*M3*		0
	M3 / Ton	0,0000	0,0000

1. Working Time Available	min	1,440	25,920
2. Planned Stoppage (a+b+c)	min	240	14,100
a. Shut Down	min	0	12,900
b. Peak Hour	min	240	1,200
c. Others	min	0	0
3. Delay Maintenance (a+b+c)	min	114	1,110
a. Daily Maintenance	min	54	476
b. Section / Pass / Grade Change	min	60	572
c. Section Setting	min	0	62
4. Break Down	min	389	2,672
a. Operation	min	389	2,366
b. Mechanical	min	0	229
c. Electrical	min	0	77
d. Material Billet Defect	min	0	0
e. Un-Controllable	min	0	0
5. Production Time Available (1-2)	min	1,200	11,820
6. Registered Delay (3+4)	min	503	3,782
7. Delay Counter (7-2)	min	503	3,782
8. Slow Operation (7-6)	min	0	0
9. Effective Production Time (5-6-8)	min	697	8,038
10. a. Nett Utilization (9/5)	%	58.08%	68.00%
b. Gross Utilization (9/1)	%	48.40%	31.01%
11. a. Nett Productivity (Sheet/(9))	Sheet/Hr	127.49	102.92
b. Gross Productivity (Sheet/(5))	Sheet/Hr	74.05	69.98
12. Electricity Consumption	MWH	3,837	54,604
	KWH/T	0	0
13. Water Consumption	M3	0	0
	M3	0	0

Activate Windows
Go to Settings to activate Windows.
